Frankie

FS Dashboard and KB Handover Overview

Frankfurt School | June 2026

The Frankie Ecosystem

Three components, this handover covers component 2 only

1

Mindsmiths Platform

AI engine · Conversation routing · WhatsApp integration · Agent logic (Onboarding, Events, Canteen, BookStack Manager) · Apache Pulsar · Kubernetes AKS

Stays on license

2

FS Dashboard & Knowledge Base

Operator dashboard · Event management · Ticketing & UCS · Conversation monitoring · BookStack knowledge base · Student-facing knowledge and support

HANDOVER TARGET

3

Frankie App

Student-facing mobile application: all Frankie capabilities natively on iOS and Android. This component is in a prototype development

Semi automatic prototype

What Frankie Does: Beyond VEA's Scope

Capabilities VEA does not cover and the Novi Sad team will need to learn from scratch

Event Management

Full lifecycle: creation, WhatsApp invites, reminder sequences, waitlists, QR check-in, attendance tracking, post-event feedback

Student Preferences

Students configure: proactive message opt-in/out, language, canteen menu subscriptions (daily/weekly), all via WhatsApp conversation

Conversation Analysis

Anonymised analysis of all student conversations; automated satisfaction reports per intake; escalation triggers

Ticketing & Assignment

Tickets opened from flagged conversations and automatically assigned to the responsible KB manager based on knowledge area

Human-in-the-Loop (UCS)

Staff can send messages that appear to students as Frankie, seamless agent handoff, invisible to the student

Operator Dashboard

Overview of all conversations, open tickets, KB performance and intake-period reporting, not available in VEA

Frankie vs VEA: Two Different Products


The Novi Sad team knows VEA. Frankie requires dedicated onboarding.

	Frankie	VEA
Audience	Students	Employees
Channel	WhatsApp (Infobip) · Frankie mobile app · Frankie website	Microsoft Teams (Copilot Studio)
Platform	Mindsmiths (proprietary, licensed) · FS Dashboard	Custom RAG pipeline (AWS + Azure serverless)
Functional scope	Events, KB, ticketing, onboarding, sentiment, QR, networking (alumni/parents), opportunity board, canteen, FS ecosystem	Q&A + HR onboarding flows
Team maintaining it	Rose (Product Owner), Mindsmiths: 3 engineers (1 senior + 2 mid) + 2 product (1 senior + 1 mid) Sawraft (dashboard, KB, design): 4 people Vedran (PM), Nives (KB) → 12 people, 3 vendors	2 Novi Sad developers (Saša, Marija) + 1 borrowed from FS IT Frankfurt (Shahnaz) + PM, PO, 1 SME

Onboarding the Novi Sad team to Frankie requires dedicated ramp-up - it cannot be treated as a simple reassignment from VEA.

Frankie Architecture

Three layers — each with a distinct ownership model

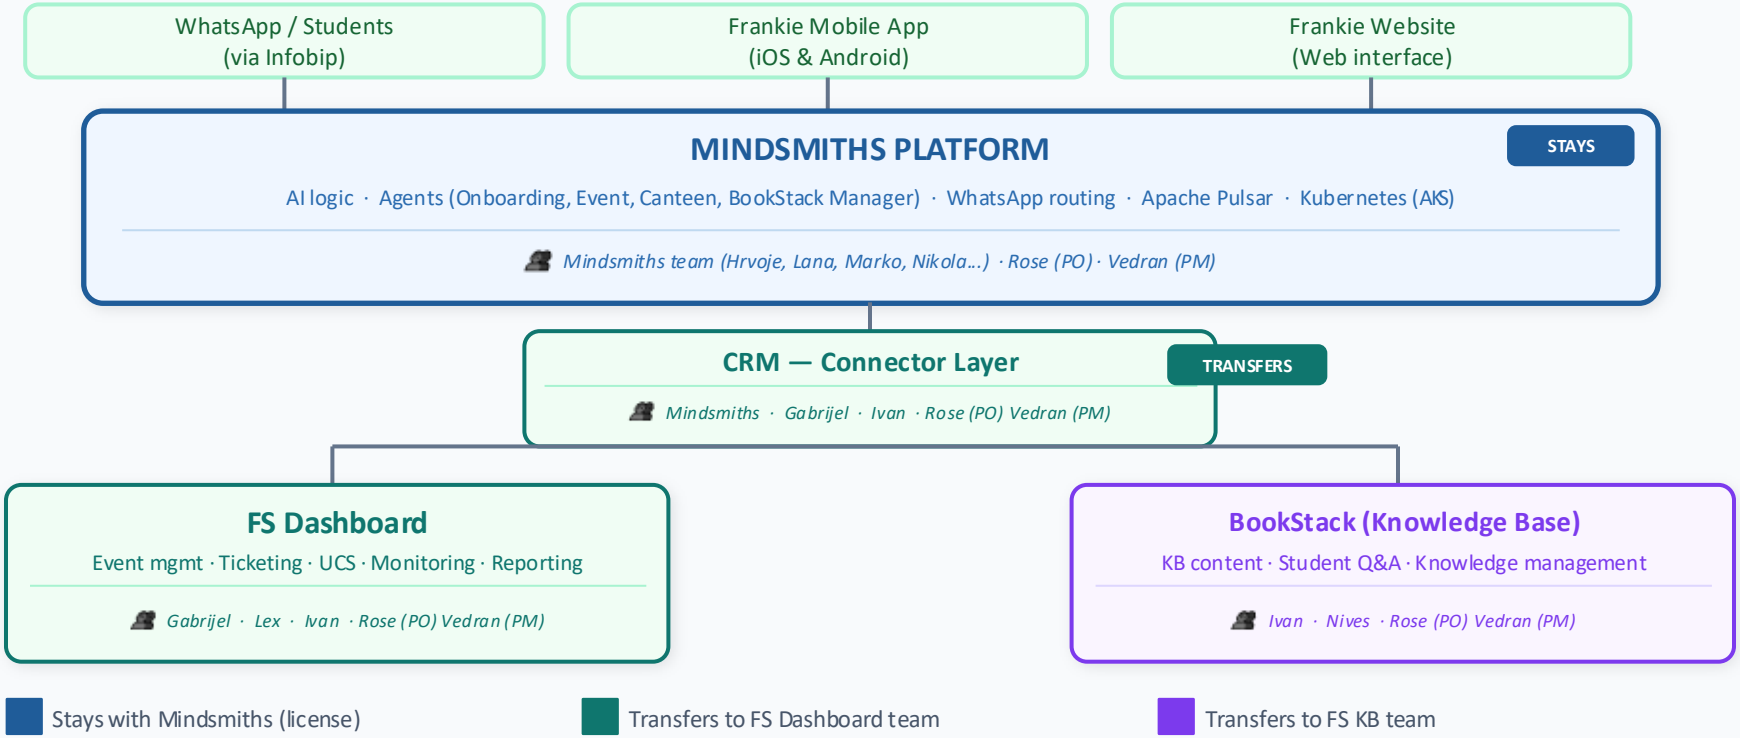

FS Needs to Hire: prerequisites for a successful handover

Two teams required before handover can begin

1 Knowledge Base Team

- Manage 1,000+ articles across all FS programmes, events and services (EN + DE)
- Full content refresh per intake cycle: programmes, events, deadlines, FAQs
- Own ticket answers: identify responsible FS stakeholder, validate, close loop
- Initiate UCS: decide when a student needs human contact; brief Dashboard team
- Write event content: descriptions, waitlist comms, post-event summaries
- Update canteen menus in BookStack (daily/weekly)
- Coordinate with 10+ FS departments (academic, admissions, student services, IT, career centre, library, alumni, events, canteen, international office…)
- Intake-period content freeze: no KB changes during peak student activity
- Monitor answer quality; flag and fix outdated content
- Multilingual content management (EN + DE)

2 FS Dashboard Team

DEVELOPMENT

- React/TypeScript FS Dashboard frontend maintenance
- CRM connector maintenance (Mindsmiths Platform integration)
- Feature development, bug fixes, security patches
- Release coordination with Mindsmiths AKS/Kubernetes cycles
- Dev / staging / production environment pipeline

OPERATIONS

- Monitor all student conversations in real-time
- Execute UCS: send message as Frankie when KB team requests
- Configure events in Dashboard: flows, invite lists, waitlists, QR codes
- Route incoming tickets to the correct KB domain owner
- Configure student preferences: opt-outs, language, canteen subscriptions
- KPI dashboards and operational reports for FS management

Proposed Transition: FS Dashboard and Knowledge Base

A structured, phased approach across four stages

Knowledge Transfer

Phase 1

1

- Structured KB handover sessions
- Dashboard codebase walkthrough
- CRM integration documentation
- FS KB team shadows live intake

Parallel Run

Phase 2

2

- FS team owns Dashboard (Frankie backup)
- FS KB team manages content (supervised)
- FS team leads sprint planning
- All ticketing routed via FS team

Supervised Handover

Phase 3

3

- FS team fully independent
- Frankie team on-call only
- KB content quality gate
- Sign-off before Frankie exits

Full FS Ownership

Phase 4

4

- Complete operational independence
- Mindsmiths on license only
- FS manages own sprint cadence
- FS runs own KB review cycle

Each phase has a formal Go/No-Go gate. The handover cannot advance before exit criteria are met for the current phase.

Key Handover Risks

Service continuity depends on a planned, phased approach

CRITICAL	Loss of institutional knowledge: the Frankie team holds five years of accumulated understanding of student behaviour, platform edge cases, seasonal operational patterns and FS stakeholder dynamics. Much of this is not formally documented.
CRITICAL	Dashboard outages with no support: the incoming FS development team will have no existing familiarity with the FS Dashboard codebase. Immediate handover without knowledge transfer leaves production bugs unsupported.
HIGH	Knowledge base degradation: without trained KB managers, content becomes outdated during intake periods, causing Frankie to give students incorrect information about events, programmes and processes.
HIGH	Mindsmiths relationship breakdown: the current team has established working relationships and escalation paths with Mindsmiths. An abrupt transition without proper onboarding of the incoming team risks delayed response times and platform miscommunication.
